


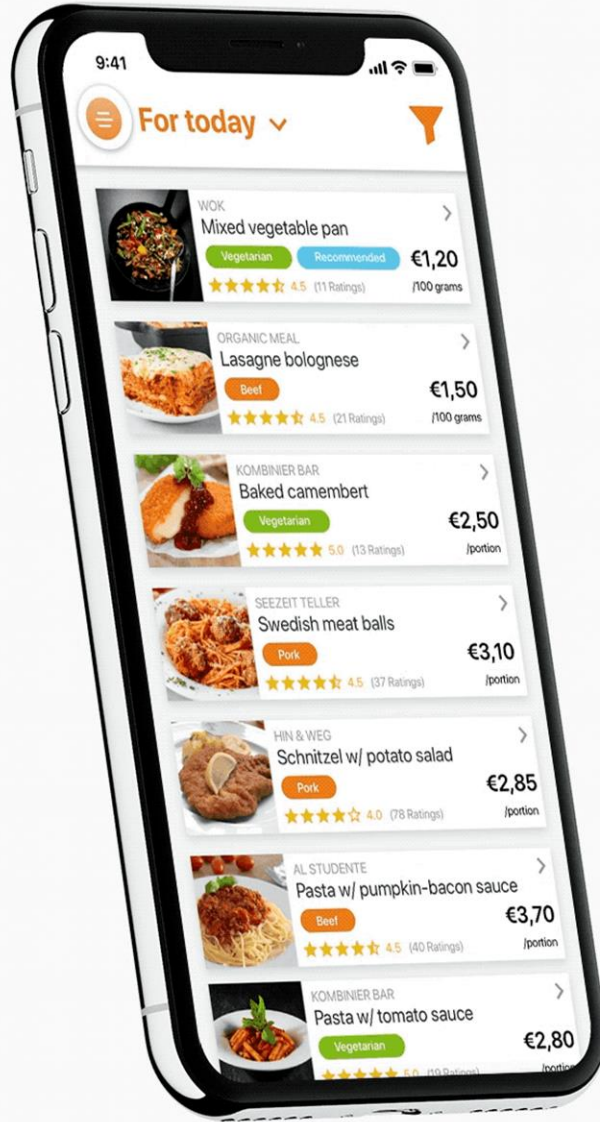

ONLINE ORDERING CANTEEN SYSTEM

for
UNILEVER

Designed by the
AGILE TEAM

APRIL 2023 COHORT

ANALYSIS OF THE EMPLOYEE CANTEEN ORDERING SYSTEM FOR




PRESENTED BY

TEAM AGILE


IMPACTED STAKEHOLDERS

The impacted stakeholders for the proposed canteen ordering system are as follows:

- Management
- Employees
- Accounts department
- IT department
- Logistics
- Quality Control
- Procurement
- Catering Department

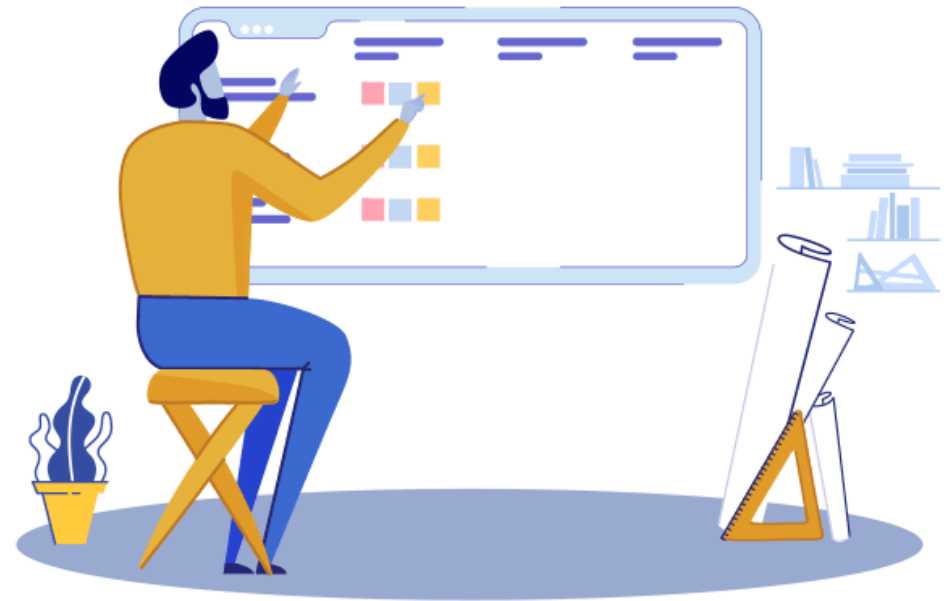

IMPACTED STAKEHOLDERS

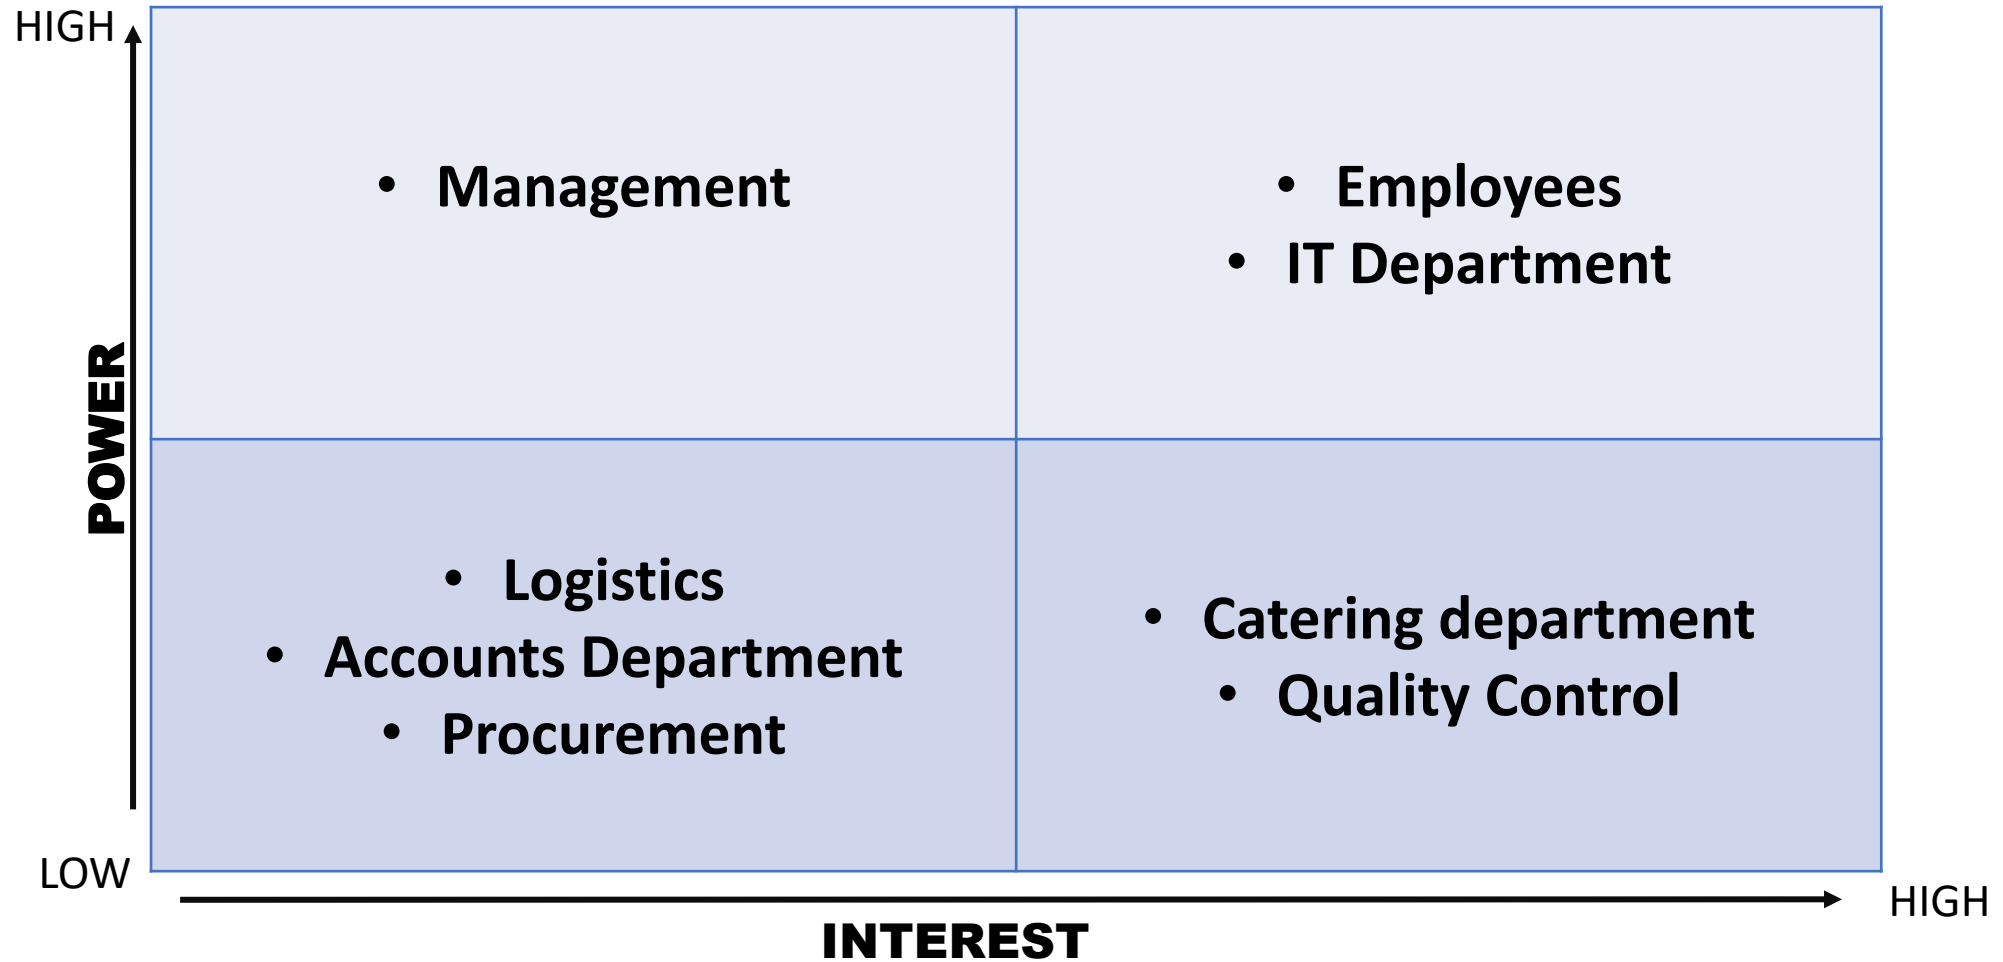

STAKEHOLDER ANALYSIS MATRIX


Stakeholder Name	Impact (Low, Medium, High)	Influence (Low, Medium, High)	Major Value	How could the Stakeholder contribute to the project?	How could the stakeholder block the project?	Strategy for engaging the stakeholder
Management	High	High	Creating a functioning ordering system, Employee productivity	By allocating funds,	By not approving funds for the project	Round table discussion, Quarterly meetings
Account Department	Low	Low	Functioning payroll system	Accurate payroll deductions	Corrupt practices	Schedule meetings and keep them informed
IT Department	Medium	High	System development and maintenance	Friendly user interface, ensure cybersecurity protection	Inadequate resource or manpower, delays in development of the project	Collaborate on requirements, provide technical expertise
Employees	High	Low	Seamless food ordering, convenient and timely food	Provision of feedback, system testing and implementation order process	Lack of patronage, resistance to change	Conduct surveys, involve UAT

STAKEHOLDER ANALYSIS MATRIX.. continued

Catering Department	High	Medium	Increase patronage and less waste	Proper meal planning, prepare dishes as per orders	Resistance to change, inadequate resources	Training and clear communication
Logistics	Low	Medium	Timely and accurate delivery	Deliver orders to Employees desk, help to identify major constraints to their work	Delivery delays, lack of Manpower and automation	Training on how to effectively read the delivery report, clear instructions, and regular coordination
Quality Control	Low	High	Ensure kitchen hygiene and Employee safety	Regular hygiene inspection and ensure compliance food safety regulations	Compromise on food safety standard	Regular updates
Procurement	High	Low	Ensure items delivered are sourced from the right suppliers at the right price	Ensuring that items ordered are delivered on time to be able to meet up with the catering department order	Compromise on quality and quantity of items delivered	Regular communication on requirement specification, submission of needs assessment

PROBLEM STATEMENT

- Monthly Food wastage.
- Limited time for lunch
- Employees have to queue for meals and also have to wait for tables to be able to eat
- Limited no of employees that can be attended to at a particular time
- Overcrowded Canteen.
- Shortage of dishes on any given day
- Unavailability of variety of meals
- Employees meal preference are unavailable
- Long turn around time for employees to have lunch

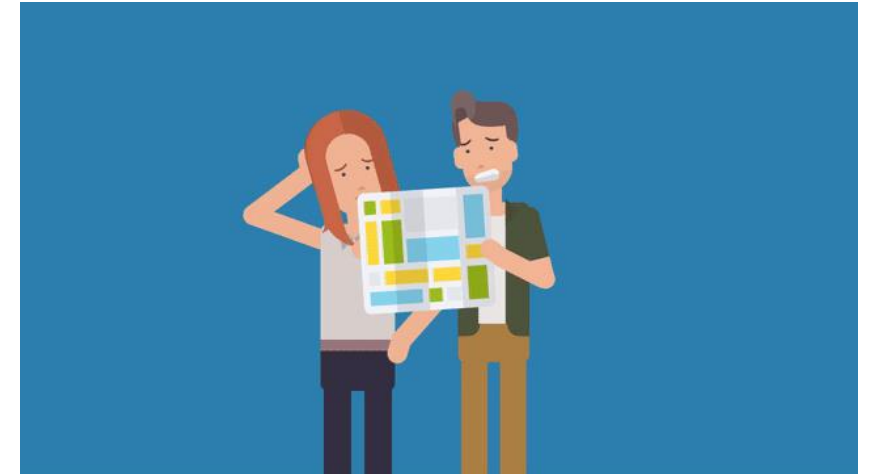

Objectives of New Canteen Ordering System

- To enable Employees to order meals on the new Unilever Canteen Ordering System
- To minimise food wastage
- Wider range of varieties of food and ensure availability
- To reduce time wastage during lunch hours
- To provide food delivery option to Employees workstation during lunch
- To provide Friendly user interface on the lunch ordering system
- Enable feedback collections to address concerns and improve the system



Objectives of the new Canteen Ordering System

- User friendly interface
- Enrolment through Salary deduction acceptance
- Ease of choice of Menu
- Can order more than one or a variety of food
- Can submit one or multiple order
- Can view previous order details including total costs
- Choice of eating at workstation or Canteen
- Management can control offers can be made easily over the Portal offering employees an improved experience.
- Cut off of food ordering on the platform by 11:00am

BUSINESS ANALYST OBJECTIVE

Business Objective 1:

The major objective of the business is to reduce canteen food wastage by a minimum of 30% within 6 months following first release.

- a. Scale: Value of food thrown away each month by examining the canteen inventory
- b. Previous - 25% wasted
- c. Must plan for: Less than 15%

Business Objective 2: Reduce canteen operating costs by 15% within 12 months, following initial release.

Business Objective 3: Increase average effective work time by 30 minutes per employee per day, within 3 months.

Business Objective 4: By making the ordering process automated and by delivering the food to the user's workstation, the canteen will be able to operate with lesser manpower.

BUSINESS CASE

SUBMITTED TO	UNILEVER MANAGEMENT	SUBMITTED BY	HEAD, BUSINESS OPERATIONS
TO THE ATTENTION OF	CEO	POINT OF CONTACT	TEAM AGILE
ADDRESS	LONDON, UNITED KINGDOM	ADDRESS	NEW BRUNSWICK, CANADA
PHONE	+44535646465	PHONE	+17064858189
EMAIL	CEO@UNILEVERUK.COM	EMAIL	Teamagile@gmail.com
DATE SUBMITTED	06/09/2023	DELIVERY METHOD	EMAIL

EXECUTIVE SUMMARY

Unilever, a leading British-Dutch FMCG company with around 1500 employees in its UK offices, is facing challenges with their current canteen ordering system. Employees experience long waiting times, limited food choices, and excessive food wastage. To address these issues and improve the overall dining experience, we propose the implementation of a new Canteen Ordering System. This System will be a notification enabled on the phone number and email will be sent once order is out for delivery. Ensure seamless integration with existing systems such as HR and payroll to enable salary deductions and data synchronization.

CURRENT SITUATION

Employees waste a significant amount of time waiting for tables during lunch hours. Long queues lead to delays in collecting food and getting a table taking about 35 minutes for each canteen user.

Limited food choices result in employees not always getting their preferred meals. Food wastage occurs due to overproduction and running out of certain items.

REASON FOR CHANGE

- The reason for change is to reduce waiting time for employees during lunch hours.
- Provide a wider variety of food choices and ensure availability.
- Minimize food wastage and improve inventory management.
- Enhance convenience and streamline the ordering and delivery process.
- Enable feedback collection to address concerns and improve the system.
- With advancements in technology, it is essential for Unilever to leverage digital solutions to enhance its internal processes. Adoption of a web-based canteen ordering system.
- By the points stated above, Unilever would be demonstrating its commitment to innovation, efficiency, and employee satisfaction, positioning itself as a progressive and forward-thinking organization.

FINDING A NEW IMPLEMENTATION

UNILEVER AGILE ORDERING SYSTEM WEBSITE

- Custom-Built Solution
- Developing a custom-built canteen ordering system tailored specifically to Unilever's requirements. This option provides maximum flexibility and customization, allowing for seamless integration with existing systems.
- This ordering system will enable the employees (Canteen User) to signup using their employment information and ID Number, since the ordering system didn't have a payment option, their user information will serve as mode of payment and the data will be securely stored and transferred directly to Unilever's Server for Payroll deductions.

REVIEW OF OPTIONS

- **Custom-Built Solution Used by Papa Jones Pizza Delivery**
- **Commercial Off-the-Shelf (COTS) Solution Used by Mc Donald**
- **Cloud-Based Solution Used by Domino's Pizza**
- **Hybrid Approach Used by KFC**

Recommended: Custom-Built Solution

POSSIBLE VENDORS

WEB-DEVELOPMENT COMPANY:

- **Avenga: Custom Web Development Company (Recommended)**
- **KitelyTech**

LOGISTICS:

- **CMS Express (Recommended)**
- **DeliveryNOW**

BENEFITS OF AN UPDATE

- Improved employee (canteen user) satisfaction and productivity by reducing waiting times and providing a convenient ordering experience.
- Enhanced food choices and availability, leading to higher employee engagement and better dining experience.
- Reduced food wastage through better inventory management and accurate order estimations.
- Streamlined order processing and delivery, ensuring timely and accurate deliveries to employees' workstations.
- Effective feedback collection for continuous improvement and addressing employee concerns.
- Cost savings through optimized inventory management and efficient resource allocation.

KEY PERFORMANCE INDICATORS

- Quarterly Projection
- Smooth and efficient Order Processing Time
- Reduction in Food Wastage Rate by 75%
- Wait Time Reduction by 75%
- Employee Satisfaction =+50%
- Menu Variety and Availability by 89%
- Cost Savings by 20%
- System Uptime, Reliability, system's availability, performance, and responsiveness, ensuring that it meets the expected service levels and minimizes disruptions to the ordering and delivery processes.

IMPLEMENTATION RISKS

Technical Risks: These risks relate to the technical aspects of implementing the new system, such as software compatibility, system integration, data migration, and infrastructure readiness. Failure to address these risks could result in system downtime, data loss, or performance issues.

Stakeholder Engagement Risks: Inadequate engagement and communication with stakeholders, including employees, canteen staff, management, and IT teams, can lead to misunderstandings, lack of support, and project delays. Effective stakeholder management is crucial to ensure alignment, gather feedback, and secure necessary resources.

Scalability and Performance Risks: The new system should be capable of scaling and accommodating future growth and increased demand. Failure to design and implement a scalable architecture can result in performance issues, system overload, and reduced user satisfaction.

Budget and Cost Risks: Poor budget planning, inaccurate cost estimation, and unforeseen expenses can lead to budget overruns, impacting the overall success of the implementation. It is crucial to have a well-defined budget, regularly monitor costs, and have contingency plans in place.

SUGGESTED VENDOR

Avenga: Custom Web Development Company Used by top 2 key industry players.

CMS Express Number 1 in the United Kingdom

OPTION COSTS

Web-Development: £17,500

Project Management & Logistics: £20,500

Total: £38,000

TECHNOLOGY MIGRATION

- **Assessment**
- **Requirements Gathering**
- **Vendor Evaluation**
- **Data Migration**
- **System Configuration and Setup**
- **Integration**
- **Testing and Quality Assurance**
- **User Training**
- **Transition and Go-Live**
- **Post-Implementation Support**

Projected timeline is **5 months** (taking available resources, urgency and current realities into account) which would be November 24, 2023.

Program Initiation (Duration: 1 week)

- Formulate the implementation team and assign roles and responsibilities.
- Conduct a kickoff meeting to align the team and set expectations. Develop a detailed implementation plan with timelines and milestones.

Requirements Analysis (Duration: 2 weeks)

- Gather and analyze the requirements for the new canteen ordering system.
- Document the functional and non-functional requirements.
- Conduct stakeholder workshops and interviews to ensure comprehensive understanding of user needs.

Vendor Selection (Duration: 2 weeks)

- Research and evaluate potential vendors based on the requirements.
- Issue request for proposals (RFPs) or requests for quotation (RFQs) to shortlisted vendors.
- Evaluate vendor proposals and conduct vendor demonstrations or proof-of-concepts.
- Select the preferred vendor based on criteria such as functionality, cost, support, and scalability.

System Development and Testing (Duration: 6 weeks)

- Develop the canteen ordering system based on the agreed-upon design and customization.
- Conduct comprehensive testing, including unit testing, integration testing, and user acceptance testing.
- Identify and resolve any issues or bugs discovered during testing.

Training and Change Management (Duration: 2 weeks)

- Develop training materials and conduct training sessions for canteen staff and employees.
- Communicate the benefits of the new system and manage the change process.
- Address any concerns or resistance to ensure smooth user adoption.

Data Migration and Go-Live Preparation (Duration: 2 weeks)

- Migrate data from the existing system to the new system, ensuring data integrity and accuracy.
- Conduct final system testing and user acceptance testing in a production-like environment.
- Prepare the system for go-live, including infrastructure setup, user account creation, and system configuration.

Go-Live and Post-Implementation Support (Duration: Ongoing)

- Deploy the new canteen ordering system in the production environment.
- Monitor system performance and address any issues or bugs that arise.
- Provide ongoing support to canteen staff and users, including troubleshooting, training updates, and system enhancements

CONCLUSION

The implementation of the new Unilever Canteen Ordering System addresses the current challenges faced by employees and the canteen management. The system will streamline the ordering process, improve efficiency, provide a wider variety of food choices, and reduce food wastage. With a positive Returns On Investment (ROI) and numerous benefits, we recommend moving forward with the project to enhance the overall dining experience and employee satisfaction at Unilever.



Roles (R,A,C,I) FOR UNILEVER CANTEEN ORDERING SYSTEM

Tasks	Business Analyst	Stakeholder	Developer	Tester	System Administrator	Trainer	Project Manager	User
Problem Statement	R	C					A	C,I
Requirement Gathering	R	C					A	I
Analyse the Unilever web page	R	I	C				A	I
Design the Canteen Ordering System	A	C	R				A	I
System Development	C	I	R				A	I
Test the new Ordering System	A	I	C	R	C		A	I
Deploy the new Ordering System	I	C	A		R		A	I
Training process participants	A	I				R	A	I


FEATURES TO BE DEVELOPED IN THE NEW SYSTEM

- User friendly interface
- Unified ordering system
- Menu management
- Delivery request
- Feedback system
- User Account Management
- Accurate payroll deductions
- Security and Privacy




Process Map Stories – AS-IS PROCESS

1. Lunch Time employee goes to Canteen
2. Check the Menu
3. Is the preferred meal Available?
4. If no, Employee leaves
5. If yes, Employee queues to order food
6. Employee collects food
7. Is a table available
8. If yes, Employee sits and have lunch
9. If no, Employee waits for available seat
10. Employee eats and go back to workstation




Unilever AS-IS Process

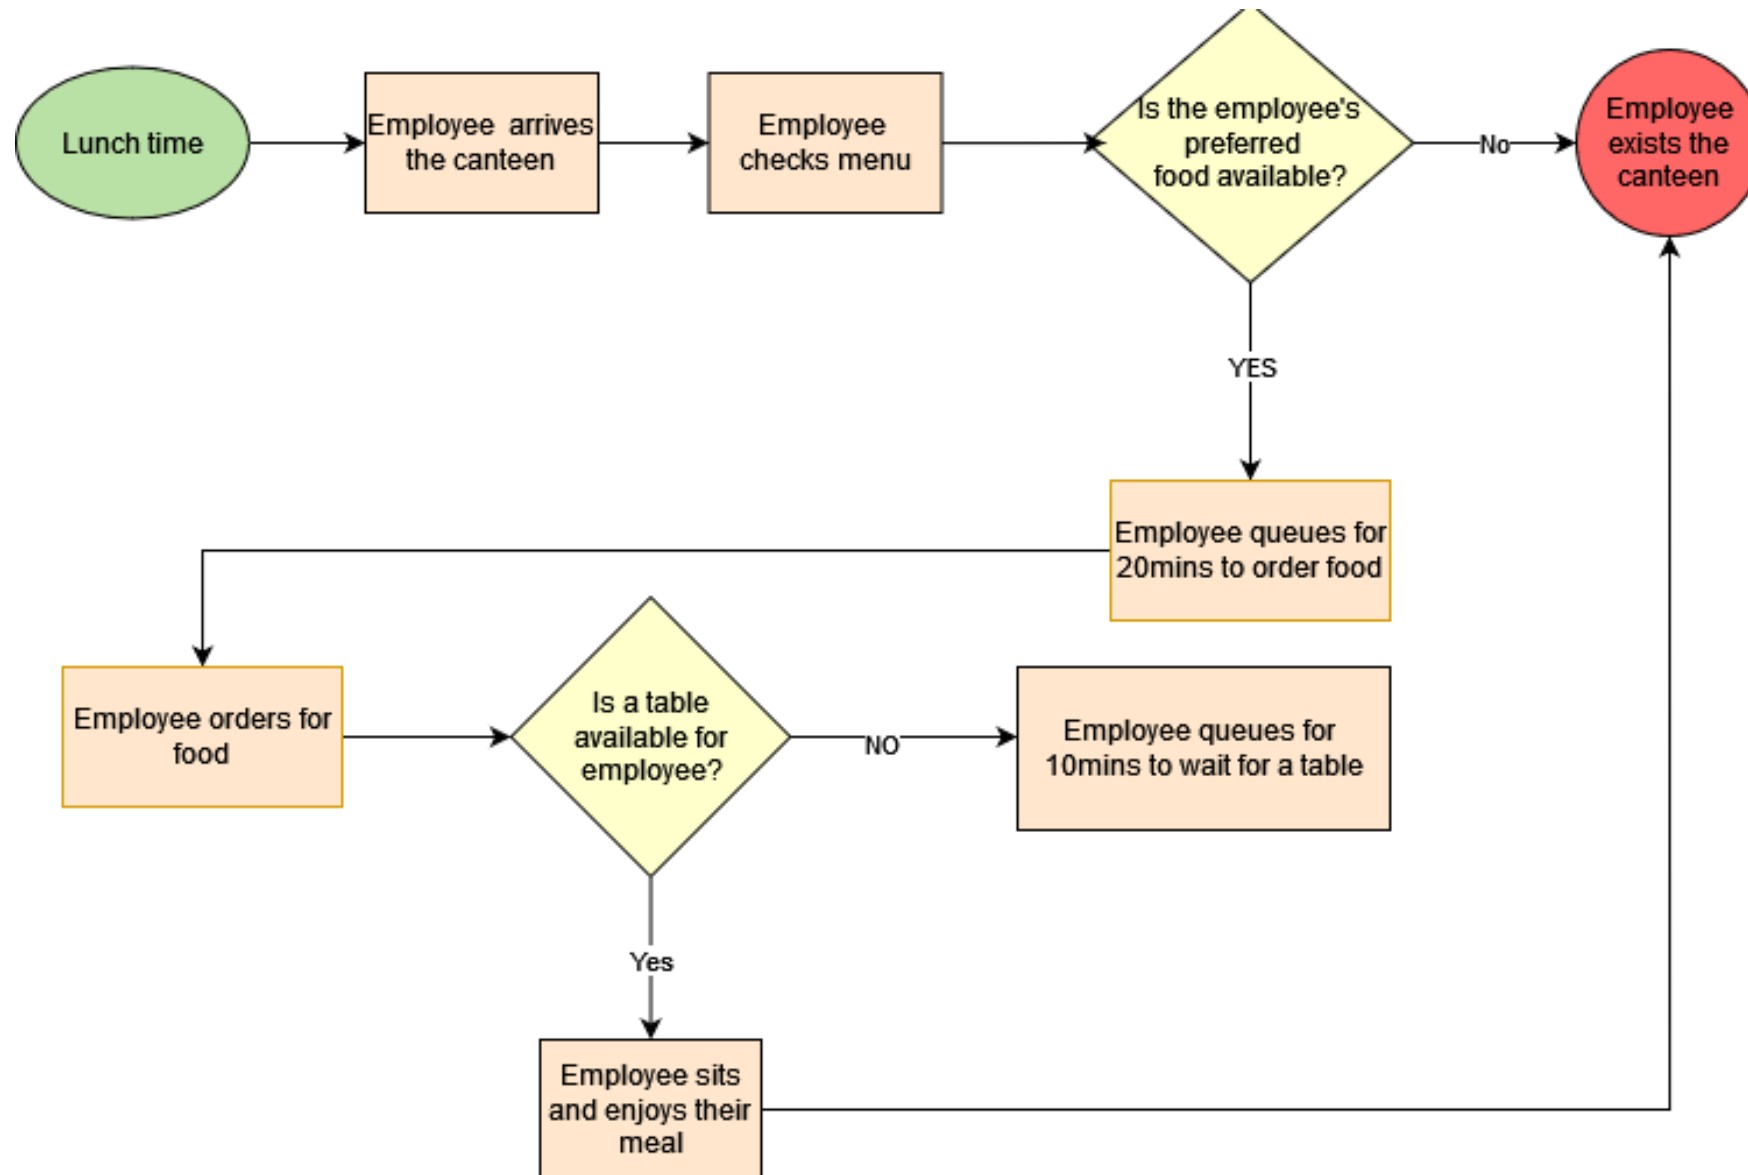


TO-BE PROCESS

1. Employee opens the Web page of the canteen ordering system
2. Ordering System presents employee with up-to-date menu plus prices
3. System will not allow employee to place order if it is after 11am
4. Canteen manager creates and updates menu
5. Employee selects dish and creates order
6. Employee edits order if needed before 11am
7. Canteen manager takes inventory of order and presents to the Chef
8. Chef prepares food
9. Canteen manager requests delivery
10. Delivery boy delivers lunch
11. Delivery boy closes online customer order
12. Employee enrolls for salary payment deduction
13. Payroll system calculates number of orders by each employee
14. Payroll system deducts money from employee's salary
15. Employee gives feedback

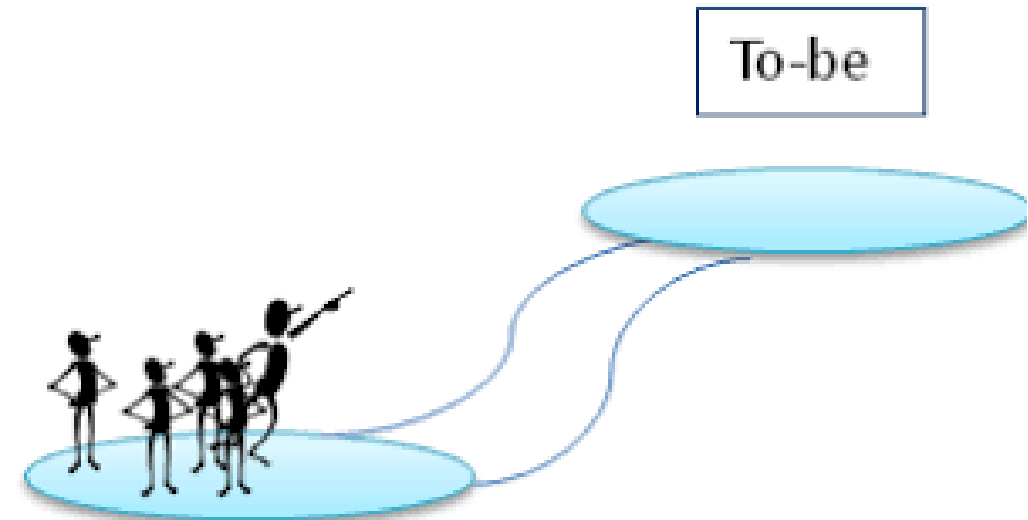

TO-BE PROCESS DIAGRAM

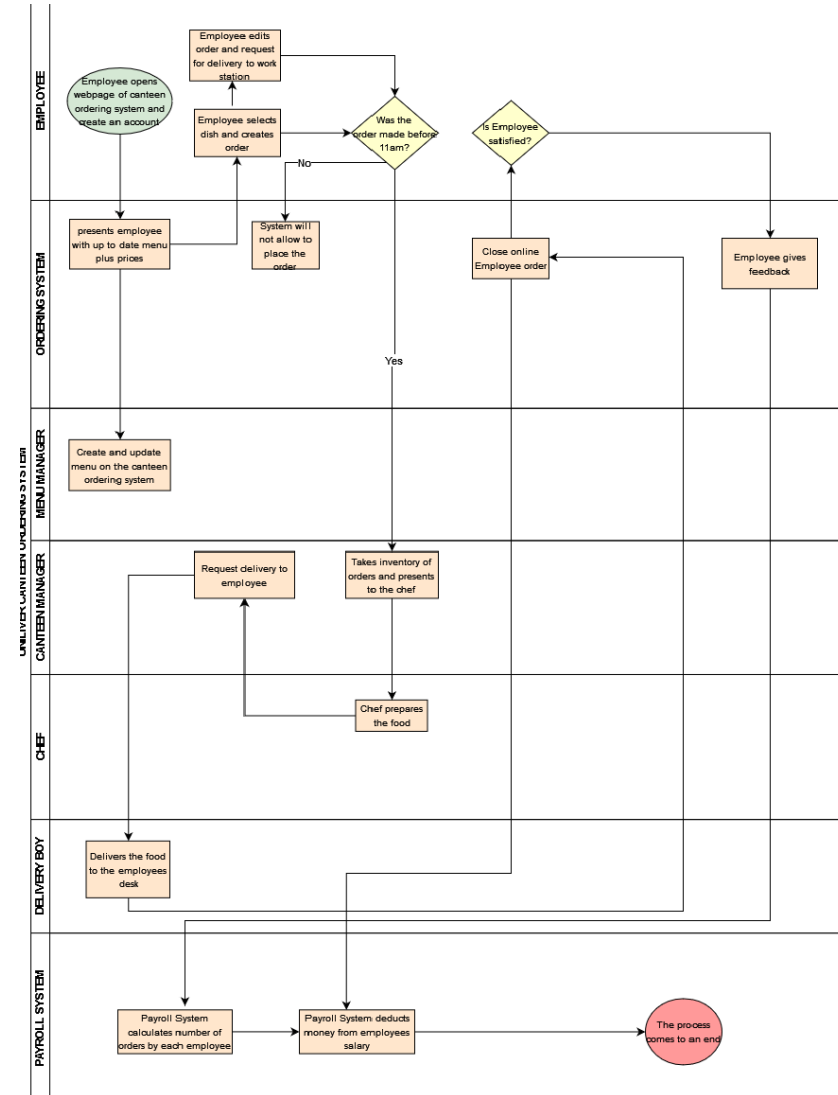

USER STORY



1. As an Employee, I want to be able to create an account using my staff ID
2. As an Employee, I want to be able to login and edit and my profile
3. As an Employee, I want to view the daily menu with available dishes and prices
4. As an Employee, I want to be able to place my order
5. As an Employee, I want to be able to request delivery to my work-station
6. As an Employee, I want to be able to provide feedback on the food quality, delivery experience and overall satisfaction



7. As a Canteen Manager, I want to be able to view and manage daily orders

8. As a Menu Manager, I want to be able to create and update daily menu

9. As a Canteen Manager, I want to be able to close order before 11am

10. As an Employee, I want to be able to receive confirmation of my order

11. As an Employee, I want to be able to enrol for salary payment deduction

12. As a Payroll system, I want to be able to calculate the total number of dishes ordered by Employee

13. As a Payroll System, I want to be able to make accurate payment deduction from Employees salary



Jira

JIRA PROJECT FOR THE PROSPOSE FOOD ORDERING SYSTEM

**The following Slides represents screenshots of our JIRA
product backlog**

k to project types

Add project details

Explore what's possible when you collaborate with your team. Edit project details anytime in project settings.

Name ^{*}

Unilever Canteen Ordering System

Access Anyone with access to scholastica76 can access and administer this project. [Upgrade your plan](#) to customize project permissions.

Key ⁱ ^{*}

UN

☐ **Connect repositories, documents, and more**

Sync your team's work from other tools with this project for better visibility, access, and automation.

Template

Change template




Scrum

◆ Jira Software

Sprint toward your project goals with a board, backlog, and timeline.

Type

Change type



Team-managed

Control your own working processes and practices in a self-contained space.

 **Unilever Canteen Order...**
Software project

 Timeline

 Backlog

 Board

DEVELOPMENT

 Code

 Project pages

 Add shortcut

 Project settings

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

Backlog

 Epic ▾

 Insights

▼ Backlog (13 issues)

0 0 0 [Create sprint](#)

 UCOS-2 1. As an Employee, I want to be able to create an account using my staff ID	TO DO ▾	
 UCOS-3 2. As an Employee, I want to be able to login and edit and my profile	TO DO ▾	
 UCOS-4 3. As an Employee, I want to view the daily menu with available dishes and prices	TO DO ▾	
 UCOS-12 4. As an Employee, I want to be able to place my order	TO DO ▾	
 UCOS-6 5. As an Employee, I want to be able to request delivery to my work station	TO DO ▾	
 UCOS-8 6. As an Employee, I want to be able to provide feedback on the food quality, delivery ex...	TO DO ▾	
 UCOS-10 7. As a Canteen Manager, I want to be able to view and manage daily orders	TO DO ▾	
 UCOS-13 8. As a Menu Manager, I want to be able to create and update daily menu	TO DO ▾	



Your work ▾

Projects ▾

Filters ▾

Dashboards ▾

Teams ▾

Apps ▾

Create

Q Search



Unilever Canteen Order...
Software project



Timeline



Backlog



Board

DEVELOPMENT



Code



Project pages



Add shortcut



Project settings

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

Backlog



SA



Epic ▾

Insights

▼ UCOS Sprint 1 17 Jul – 31 Jul (4 issues)

0

0

0

Start sprint



To be able to create the home page the web-site.



UCOS-2 1. As an Employee, I want to be able to create an account using my staff ID

TO DO ▾



UCOS-3 2. As an Employee, I want to be able to login and edit and my profile

TO DO ▾



UCOS-4 3. As an Employee, I want to view the daily menu with available dishes and prices

TO DO ▾



UCOS-12 4. As an Employee, I want to be able to place my order

TO DO ▾



+ Create issue

▼ Backlog (9 issues)

0

0

0

Create sprint

 Unilever Canteen Order...
Software project

PLANNING

 Timeline

 Backlog

 Board

DEVELOPMENT

 Code

 Project pages

 Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering System

UCOS Sprint 1

To be able to create the home page the web-site.

⚡ ☆ ⌚ 12 days remaining **Complete sprint** ⋮

SA 

GROUP BY **None ▾**  Insights

TO DO 1 ISSUE

4. As an Employee, I want to be able to place my order

 UCOS-12



IN PROGRESS 1 ISSUE

3. As an Employee, I want to view the daily menu with available dishes and prices

 UCOS-4



DONE 2 ISSUES ✓

1. As an Employee, I want to be able to create an account using my staff ID

 UCOS-2



2. As an Employee, I want to be able to login and edit my profile

 UCOS-3





Your work ▾

Projects ▾

Filters ▾

Dashboards ▾

Teams ▾

Apps ▾

Create

Search



Unilever Canteen Order...

Software project

PLANNING



Timeline



Backlog



Board

DEVELOPMENT



Code



Project pages



Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

UCOS Sprint 1

To be able to create the home page the web-site.



SA



12 days remaining

Complete sprint



GROUP BY

None ▾

Insights

O

IN PROGRESS

DONE 4 ISSUES ✓



1. As an Employee, I want to be able to create an account using my staff ID



UCOS-2



2. As an Employee, I want to be able to login and edit and my profile



UCOS-3





Your work ▾

Projects ▾

Filters ▾

Dashboards ▾

Teams ▾

Apps ▾

Create

Q Search



Unilever Canteen Order...
Software project

PLANNING



Timeline



Backlog



Board

DEVELOPMENT



Code



Project pages



Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

Backlog



Epic ▾



Insights

▼ UCOS Sprint 2 2 Aug – 16 Aug (4 issues)

0 0 0

Start sprint



Create menu and place orders.



UCOS-6 5. As an Employee, I want to be able to request delivery to my work station

TO DO ▾



UCOS-8 6. As an Employee, I want to be able to provide feedback on the food quality, delivery ex...

TO DO ▾



UCOS-10 7. As a Canteen Manager, I want to be able to view and manage daily orders

TO DO ▾



UCOS-13 8. As a Menu Manager, I want to be able to create and update daily menu

TO DO ▾



+ Create issue



▼ Backlog (5 issues)

0 0 0

Create sprint



Your work ▾

Projects ▾

Filters ▾

Dashboards ▾

Teams ▾

Apps ▾

Create

Q Search



Unilever Canteen Order...
Software project

PLANNING



Timeline



Backlog



Board

DEVELOPMENT



Code



Project pages



Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

UCOS Sprint 2

Create menu and place orders.



24 days remaining

Complete sprint



SA



GROUP BY

None ▾



Insights

TO DO 1 ISSUE

8. As a Menu Manager, I want to be able to create and update daily menu

UCOS-13



IN PROGRESS 1 ISSUE

7. As a Canteen Manager, I want to be able to view and manage daily orders

UCOS-10



DONE 2 ISSUES ✓

5. As an Employee, I want to be able to request delivery to my work station

UCOS-6



6. As an Employee, I want to be able to provide feedback on the food quality, delivery experience and overall satisfaction



Unilever Canteen Order...
Software project

PLANNING

 Timeline

 Backlog

 Board

DEVELOPMENT

 Code

 Project pages

 Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering System

UCOS Sprint 2

Create menu and place orders.





 24 days remaining

Complete sprint



GROUP BY

None ▾

 Insights

IN PROGRESS 1 ISSUE

8. As a Menu Manager, I want to be able to create and update daily menu

 UCOS-13



DONE 3 ISSUES ✓

5. As an Employee, I want to be able to request delivery to my work station

 UCOS-6



6. As an Employee, I want to be able to provide feedback on the food quality, delivery experience and overall satisfaction





Your work ▾

Projects ▾

Filters ▾

Dashboards ▾

Teams ▾

Apps ▾

Create

Search



Unilever Canteen Order...

Software project

PLANNING



Timeline



Backlog



Board

DEVELOPMENT



Code



Project pages



Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

UCOS Sprint 2

Create menu and place orders.



SA



24 days remaining

Complete sprint



GROUP BY

None ▾

Insights

IN PROGRESS

DONE 4 ISSUES ✓



5. As an Employee, I want to be able to request delivery to my work station

UCOS-6



6. As an Employee, I want to be able to provide feedback on the food quality, delivery experience and overall satisfaction

 **Unilever Canteen Order...**
Software project

PLANNING

 Timeline

 Backlog

 Board

DEVELOPMENT

 Code

 Project pages

 Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

Backlog

 Epic ▾

 Insights

▼ UCOS Sprint 3 17 Aug – 7 Sep (5 issues)

000 **Start sprint** ⋮

Ensure Effective Delivery , Accurate Deductions and Feedback.

- | | |
|--|---|
|  UCOS-9 9. As a Canteen Manager, I want to be able to close order before 11am | TO DO ▾  |
|  UCOS-5 10. AS an Employee, I want to be able to receive confirmation of my order | TO DO ▾  |
|  UCOS-1 11. As an Employee, I want to be able to enrol for salary payment deduction | TO DO ▾  |
|  UCOS-11 12. As a Payroll system, I want to be able to calculate the total number of dishes ordere... | TO DO ▾  |
|  UCOS-7 13. As a Payroll System, I want to be able to make accurate payment deduction from Em... | TO DO ▾  |

+ Create issue



Your work ▾

Projects ▾

Filters ▾

Dashboards ▾

Teams ▾

Apps ▾

Create

Q Search



Unilever Canteen Order...
Software project

PLANNING



Timeline



Backlog



Board

DEVELOPMENT



Code



Project pages



Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

UCOS Sprint 3

Ensure Effective Delivery , Accurate Deductions and Feedback.



40 days remaining

Complete sprint



SA



GROUP BY

None ▾



Insights

TO DO 2 ISSUES

12. As a Payroll system, I want to be able to calculate the total number of dishes ordered by Employee

UCOS-11



13. As a Payroll System, I want to be able to make accurate payment deduction from Employees salary

IN PROGRESS 1 ISSUE

11. As an Employee, I want to be able to enrol for salary payment deduction

UCOS-1



DONE 2 ISSUES ✓

9. As a Canteen Manager, I want to be able to close order before 11am

UCOS-9



10. AS an Employee, I want to be able to receive confirmation of my order

UCOS-5



Unilever Canteen Order...
Software project

PLANNING

Timeline

Backlog

Board

DEVELOPMENT

Code

Project pages

Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

UCOS Sprint 3

Ensure Effective Delivery , Accurate Deductions and Feedback.

40 days remaining
Complete sprint

GROUP BY
None ▾
 Insights

TO DO

IN PROGRESS 2 ISSUES

DONE 3 ISSUES ✓

12. As a Payroll system, I want to be able to calculate the total number of dishes ordered by Employee

UCOS-11

13. As a Payroll System, I want to be able to make accurate payment deduction from Employees salary

9. As a Canteen Manager, I want to be able to close order before 11am

UCOS-9

10. AS an Employee, I want to be able to receive confirmation of my order

UCOS-5

 Unilever Canteen Order...
Software project

PLANNING

 Timeline

 Backlog

 Board

DEVELOPMENT

 Code

 Project pages

 Add shortcut

You're in a team-managed project

[Learn more](#)

Projects / Unilever Canteen Ordering Sytem

UCOS Sprint 3

Ensure Effective Delivery , Accurate Deductions and Feedback.



40 days remaining

Complete sprint



Q



GROUP BY

None ▾

 Insights

IN PROGRESS

DONE 5 ISSUES ✓



9. As a Canteen Manager, I want to be able to close order before 11am



UCOS-9



10. AS an Employee, I want to be able to receive confirmation of my order



UCOS-5



**THANK
YOU!**
